

TechLauncher 2026 S1 Key Criteria Evidence Review

Hyperspectral Image Inspector

Team LEAF · Ryan Foote · Guochen Wang · Pengyun Wang · Jingyi Sun

14 August 2026

How this deck is organised

Each following slide covers one rubric category. Every claim is backed by a specific Jira ticket or Confluence page

Category	Bullets	Status snapshot		
Stakeholder Engagement	7	5 solid	2 gaps	
Planning & Organisation	10	6 solid	3 gaps	1 improving
Execution & Quality	8	6 solid	2 gaps	
Reflection & Improvement	6	2 solid	4 gaps	

1. Stakeholder Engagement

Regular meetings in The Hive **SOLID**

Fixed weekly cadence — Client Fri 10am, Tutor Fri 2:30pm.
Client Mtg #8: full attendance (4 team + client Tao Hu). 8 meeting logs to date.

Detailed progress & challenge updates **SOLID**

Weekly Report covers requirements closure, MVC split, 17 new tickets, 7 PRs merged. Client walked through open questions live, not a "finished" plan.

Clarify expectations & flag risks early **SOLID**

Design doc "Residual Open Questions": ground-truth dataset availability, GPU hardware, sensor model — named as needing the client, not guessable.

Record meeting minutes + action items **SOLID**

8 Confluence pages, Date/Participants/Goals/Notes template.
Nuance: a numbered action-item list per meeting is still maturing.

Assign & manage tasks from feedback **SOLID**

Client Mtg #8 → Planning Doc Q&A → Design/FR doc → 17 new tickets (LEAF-104–120) same week. Gap: not yet repeatable every meeting.

Report action-item status to stakeholders **GAP**

"Not yet a formal, recurring practice; we report progress narratively rather than against a tracked action-item list." Named as next-sprint improvement.

Improve relationships / address conflicts **SOLID**

No conflicts to date; practice is timely, honest reporting (incl. "not started" items). Risk register tracks "miscommunication with client" (Med/High) with mitigation.

2. Planning & Organisation

Project Vision with stakeholders **SOLID**

Design Overview & FR doc built from Planning Doc Q&A + Client Mtg #8: problem statement, system overview, FRs, NFRs, Phase 2 backlog, open questions.

Tool to plan & manage project **SOLID**

Jira (Epic LEAF-84 + Sprint board) rather than GitLab — functionally equivalent, different vendor. GitHub for source control. Currently Sprint 4 (30 Jul–14 Aug).

Record goals & milestones **SOLID**

Epic → Story → Subtask hierarchy (e.g. LEAF-104, LEAF-93). FR doc §7 "Traceability" links every requirement to its Confluence source and Jira ticket.

Maintain a backlog **PARTIAL**

100+ issues; grew by 21 in one week. Scenario & User Story pages exist.

Tickets use Given/When/Then, not formal persona format; no standalone test tickets yet.

Map PBIs to goals & milestones **SOLID**

LEAF-104 → FR§3.2 Visualization, LEAF-105 → FR§3.4 Calibration, LEAF-107 → FR§3.5 Segmentation — each traced to Epic LEAF-84.

2. Planning & Organisation

Planning Poker for estimates **GAP**

No estimation yet — all 17 new tickets have no story points. Still using the "simple deadlines" early-stage allowance. Next step: size sprint tickets as a team.

Assign PBIs, set deadlines **IMPROVING**

7 Aug: tickets unassigned. 14 Aug: all 8 Sprint 4 items now carry a named assignee matching the Model/View split (e.g. LEAF-104 → Pengyun, LEAF-106 → Guochen).

Prioritise backlog by goals/needs **SOLID**

Deliberate cuts: Supervised classification deferred (client dataset question unresolved); Super-Resolution de-risked via research spike LEAF-112 first.

Identify & manage risks **SOLID**

7 risks tracked, each with a named owner — e.g. miscommunication (Med/High), limited Friday-only dev time (High/High), dependency delays (Med/High). Reviewed weekly.

Monitor velocity for future planning **GAP**

No velocity tracked yet — direct consequence of the estimation gap above. Becomes possible once Planning Poker sizing starts next sprint.

3. Execution & Quality

PM tool for task management **SOLID**

Jira Epic LEAF-84 + Sprint 4 board hold every Story, Task, Subtask, Bug — no parallel spreadsheet or ad hoc list.

Version control practices **SOLID**

7 scoped PRs this week (#5–11); 15 merged to date. Commit messages reference the originating Jira ticket (e.g. LEAF-121).

Keep milestones/PBIs up to date **SOLID**

FR audit tags each requirement Done/Partial/UI only/Not started against the real codebase — an honest audit, not a status guess.

CI/CD pipelines **GAP**

No CI/CD configuration in the repo (no .github/workflows). Named as a genuine next step — even a lint/build check would help.

3. Execution & Quality

Unit/integration testing **GAP**

NFR specifies vegetation indices validated within 1% tolerance vs. sample-img/, but most Model-layer work is "Not started" — top priority for Jingyi/Pengyun next sprint.

Monitor & respond to challenges **SOLID**

PR #11 fixed a Classification-tab regression the same week. Super-Resolution spike (LEAF-112) time-boxes the riskiest area proactively.

Peer review of code/docs/design **SOLID**

Every merged PR this week had human approval (Ryan/Guochen cross-review) plus a bot review (Copilot/CodeRabbit). Design doc reviewed against the live codebase too.

Summarise impact of work completed

SOLID

One tool now covers Visualization, Calibration, Super-Resolution, Classification — replacing crash-prone/basic tools for APPN operators and researchers.

4. Reflection & Improvement

Seek tutor/stakeholder feedback regularly **SOLID**

Weekly tutor meeting (Fri 2:30pm) alongside weekly client meeting (Fri 10am). Weekly Report for Tutor exists specifically to feed this loop.

PBIs from retro/review actions **GAP**

Blocked on the two gaps above — no retro/review actions exist yet to convert into PBIs. Natural next step once Sprint 4 review/retro happens.

Sprint review each sprint **GAP**

No formal sprint review held yet — Client Mtg #8 served a similar function informally. Sprint 4 closes 14 Aug (today); a proper review is planned before it does.

Record clear responses to feedback **SOLID**

This week's "Rubric Self-Assessment" is the team's first explicit, point-by-point response to an external feedback framework (the rubric itself).

Sprint retrospective each sprint **GAP**

One retro logged (Sprint 1, 24 Apr) but the Start/Stop/Keep template was never filled in. None run for Sprints 2–4; a real retro planned before next sprint boundary.

Individual reflections (optional) **DEFERRED**

Not yet started — deprioritised in favour of the higher-priority gaps above. Explicitly optional per the rubric.

Where this leaves us

Strong and evidenced

- Weekly client + tutor meeting cadence, fully attended
- Client feedback → design doc → Jira tickets pipeline
- Living risk register with owners, reviewed weekly
- PR-based workflow with dual (human + bot) review
- Honest, audited FR status rather than optimistic tracking


Named gaps, with a plan

- Planning Poker / story points / velocity — start next sprint
- CI/CD pipeline — even a lint/build check is the next floor
- Model-layer unit tests against `sample-img/` — top priority for next sprint's Model owners
- Formal sprint review + retrospective — due before Sprint 4 closes today

Appendix — UI Evolution

Same four-module tool (Visualization, Super-Resolution, Calibration, Classification), rebuilt with a consistent theme and navigation.

Initial prototype

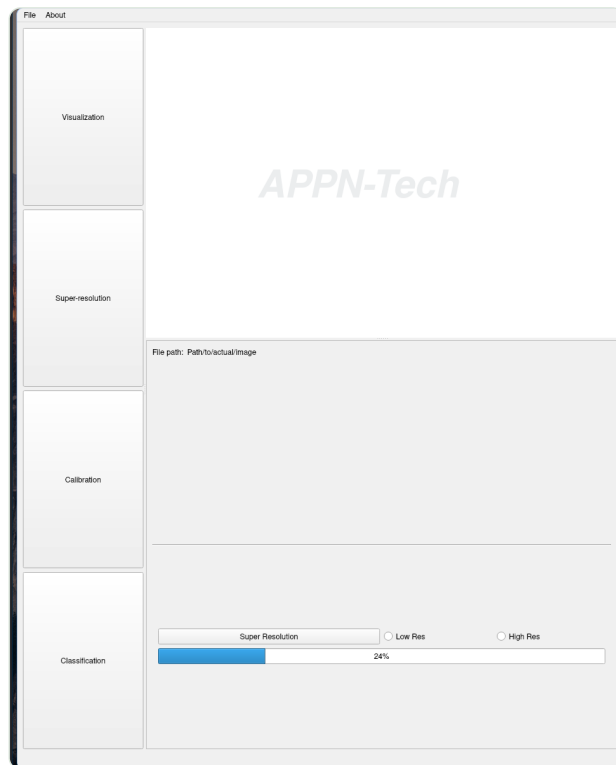

Stacked sidebar buttons, unthemed grey panels

Sprint 4 build



Horizontal tab bar, consistent theme, aligned controls

Pull Requests

15 PRs merged since 22 May 2026. 14 in Hyperspectral-Image-Inspector, plus 1 bug-fix PR in the Leaf-Analyzer-Pattern-Generation repo.

Date	PR	Title	Repo
7 Aug	#15	LEAF-121 file to navigation bar	Inspector
7 Aug	#14	Requirements update	Inspector
7 Aug	#13	Remove dead ui/panels/ swappable-panel code	Inspector
7 Aug	#12	feat(ui): refine tab interactions and viewer alignment	Inspector
7 Aug	#11	feat(ui): restore classification tab	Inspector
31 Jul	#10	LEAF-96 Super Resolution buttons	Inspector
31 Jul	#9	feat(ui): add calibration tab to the main window	Inspector
31 Jul	#32	LEAF-98 Fix text scaling saving (<i>bug fix</i>)	Pattern Gen
31 Jul	#7	LEAF-94 Visualization panel framework	Inspector
31 Jul	#6	LEAF-91 Tabular UI Foundations	Inspector
31 Jul	#5	LEAF-92 apply a theme to the app	Inspector
22 May	#4	LEAF-89 fix image opening	Inspector
22 May	#3	LEAF-88 architecture overview file	Inspector
22 May	#2	LEAF-87 Claude initial OOP rewrite	Inspector
22 May	#1	fix: resolve file path issue and correct file naming typo	Inspector

Jira Tickets

40 tickets created or modified since 22 May 2026 (of 109 in the project overall).

Where the activity sits

LEAF-84 · Hyperspectral IN PROGRESS

31 tickets touched — the epic itself, its 18 direct children, and 12 further subtasks

LEAF-6 / LEAF-13 · Design Process & MVP DONE

9 tickets touched — edits/status updates on already-completed early-phase work

By type (40 total)

Task	18
Subtask	12
Story	6
Epic	3
Bug	1

By status

22 Done (PR merged)

1 In Progress 17 To Do
